COM0463 IT Project Management

Spring 2025

Information Technology Project Management 4e

Chapter 4-The Project Team

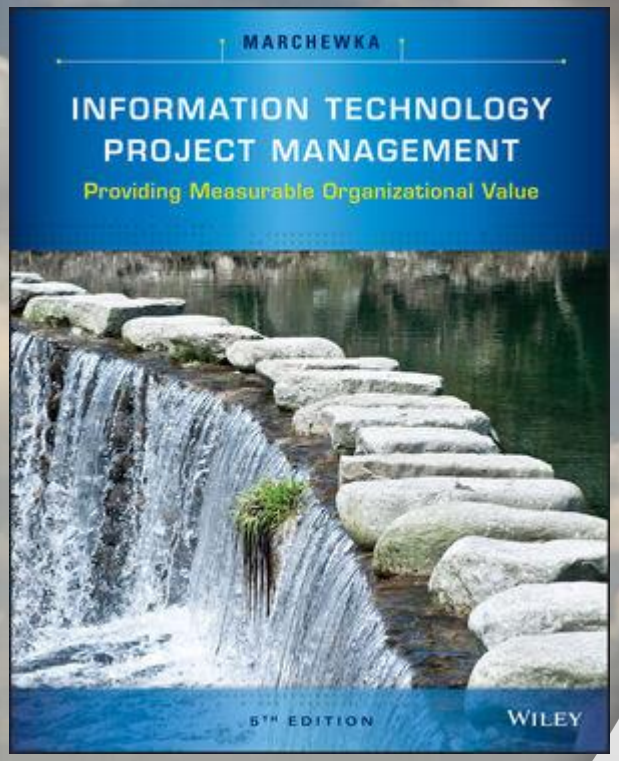

Time	Lecture	Note
14:00-14:45	Hour-1	Theory & Practices
15:00-15:45	Hour-2	Theory & Practices
16:00-16:45	Hour-3	Theory & Practices
17:00-17:45	Hour-4	Theory & Practices

Yusuf Altunel, PhD

IKU Department of Computer Engineering

y.altunel@iku.edu.tr

Learning Objectives

Formal organizations	• Describe major types of formal organizational structures
Alternatives	• Functional, pure project, matrix
Advantages & disadvantages	• For various organizational structures
Informal Organizations	• Describe the informal organization.
Stakeholder analysis	• Develop a stakeholder analysis.
Work group vs. Team	• Describe the difference between a work group & a team.
Knowledge management	• Describe and apply a basis for knowledge management
Learning cycles	• the concept of learning cycles • lessons learned.
HR Plan	• Develop Human Resource Plan
Project Team	• Acquire, Develop, & Manage the Project Team

Copyright 2012 John Wiley & Sons, Inc.

Knowledge Areas	Project Management Process Groups				
	Initiating	Planning	Executing	Monitoring and Controlling	Closing
[4] Project Integration Management	4.1 Develop Project Charter	4.2 Develop Project Management Plan	•4.3 Direct and Manage Project Work •4.4 **Manage Project Knowledge**	•4.5 Monitor and Control Project Work •4.6 Perform Integrated Change Control	4.7 Close Project or Phase
[5] Project Scope Management		•5.1 Plan Scope Management •5.2 Collect Requirements •5.3 Define Scope •5.4 Create WBS		•5.5 Validate Scope •5.6 Control Scope	
[6] Project **Schedule** Management		**•6.1 Plan Schedule Management** **•6.2 Define Activities** **•6.3 Sequence Activities** **•6.4 Estimate Activity Durations** **•6.5 Develop Schedule**		**6.6 Control Schedule**	
[7] Project Cost Management		•7.1 Plan Cost Management •7.2 Estimate Costs •7.3 Determine Budget		7.4 Control Costs	
[8]Project Quality Management		8.1 Plan Quality Management	8.2 **Manage Quality**	8.3 Control Quality	
[9]Project **Resource** Management		•9.1 Plan Resource Management •9.2 **Estimate Activity Resources**	•9.3 Acquired **Resources** •9.4 Develop **Team** •9.5 Manage **Team**	9.6 **Control Resources**	
[10] Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 **Monitor Communications**	
[11] Project Risk Management		•11.1 Plan Risk Management •11.2 Identify Risks •11.3 Perform Qualitative Risk Analysis •11.4 Perform Quantitative Risk Analysis •11.5 Plan Risk Responses	11.6 **Implement Risk Responses**	11.7 **Monitor** Risks	
[12] Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
[13] Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder **Engagement**	13.3 Manage Stakeholder Engagement	13.4 **Monitor** Stakeholder Engagement	

Develop Human Resource Plan

staff management plan

- identifies and documents
- the reporting relationships

team member's

- role
- responsibility
- required skills

HR Availability

- Confirms specific human resources will be available
- to work on the project

Copyright 2012 John Wiley & Sons, Inc.

Develop Project Team

Team Improvement

- Facilities to improve the team

Improvements

- the competencies of the project team
- their interactions
- the overall team environment

Copyright 2012 John Wiley & Sons, Inc.

Manage the Project Team

tracking	the project team's performance
providing	feedback
resolving	interpersonal issues
managing	organizational change

Copyright 2012 John Wiley & Sons, Inc.

The Formal Organization

Formal

- groupings
- specializations

Published Lines of

- Authority
- Responsibilities
- Reporting Relationships
- Communication
- Decision-Making

Copyright 2012 John Wiley & Sons, Inc.

Organizational Structure

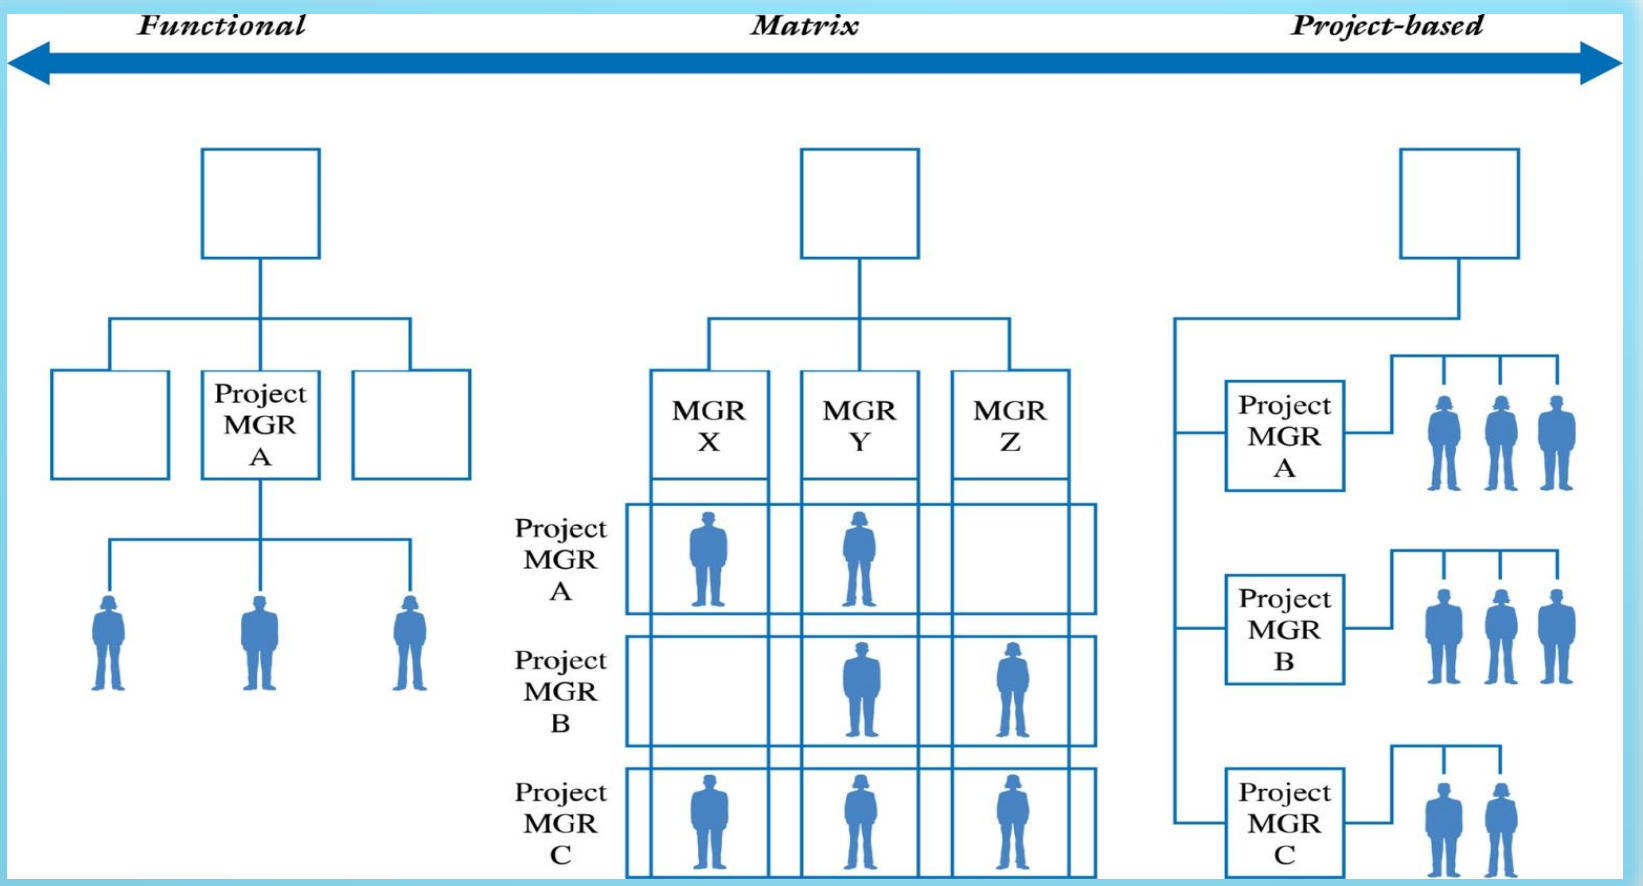

Copyright 2012 John Wiley & Sons, Inc.

The Functional Organization

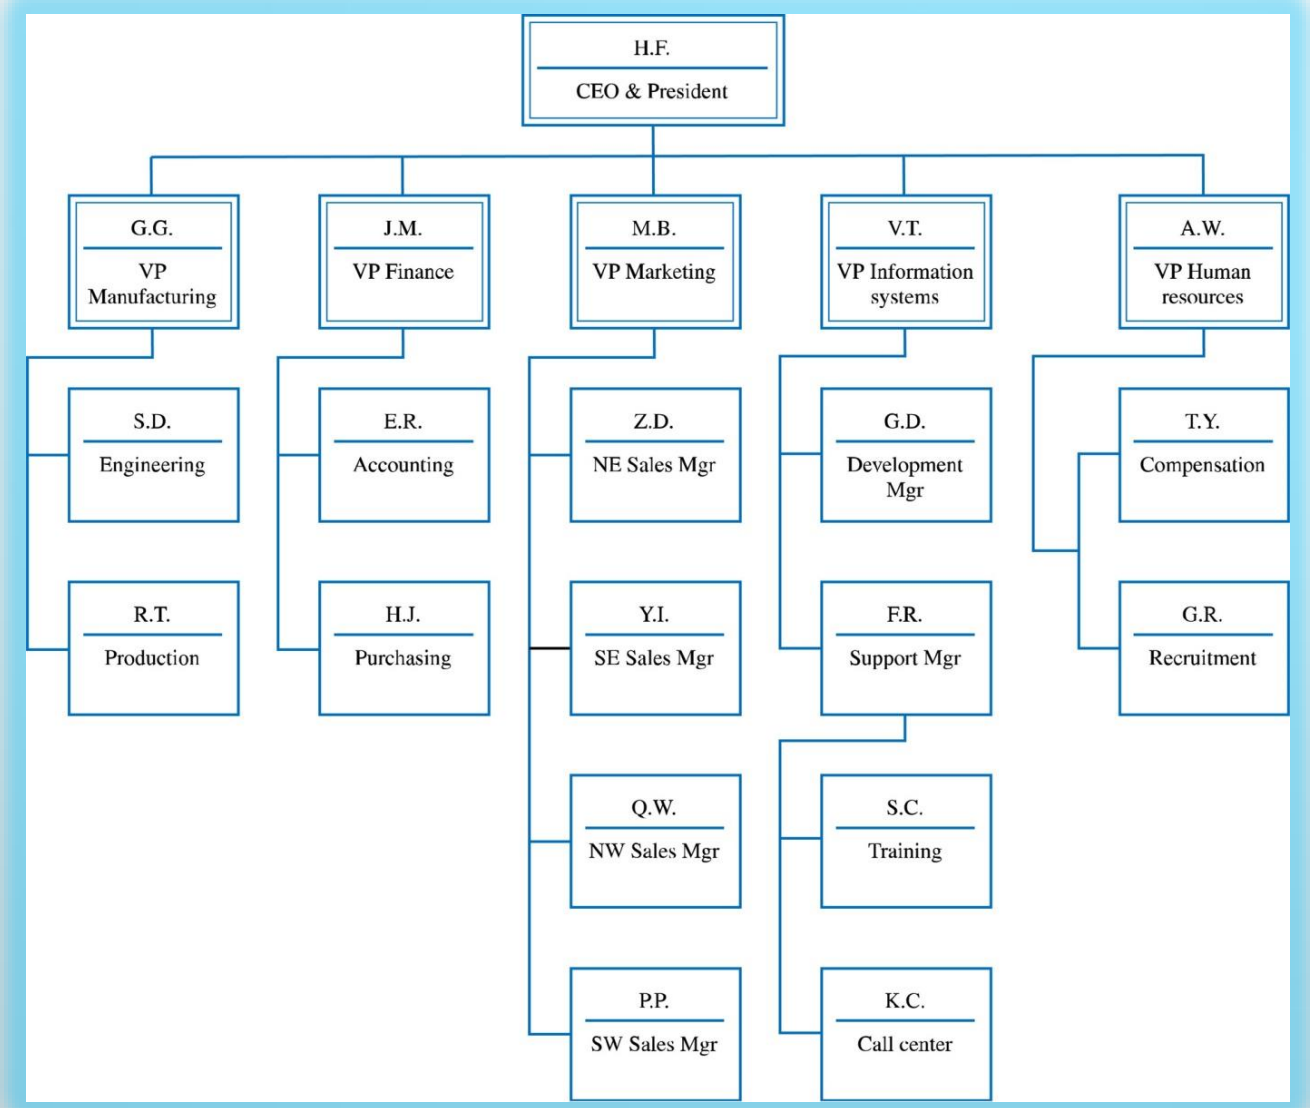

Copyright 2012 John Wiley & Sons, Inc.

THE FUNCTIONAL ORGANIZATION

Advantages

- Increased Flexibility
- Breadth & Depth of Knowledge & Experience
- Less Duplication

Determining Authority & Responsibility

- Poor Response Time
- Poor Integration

Copyright 2012 John Wiley & Sons, Inc.

The Project Organization

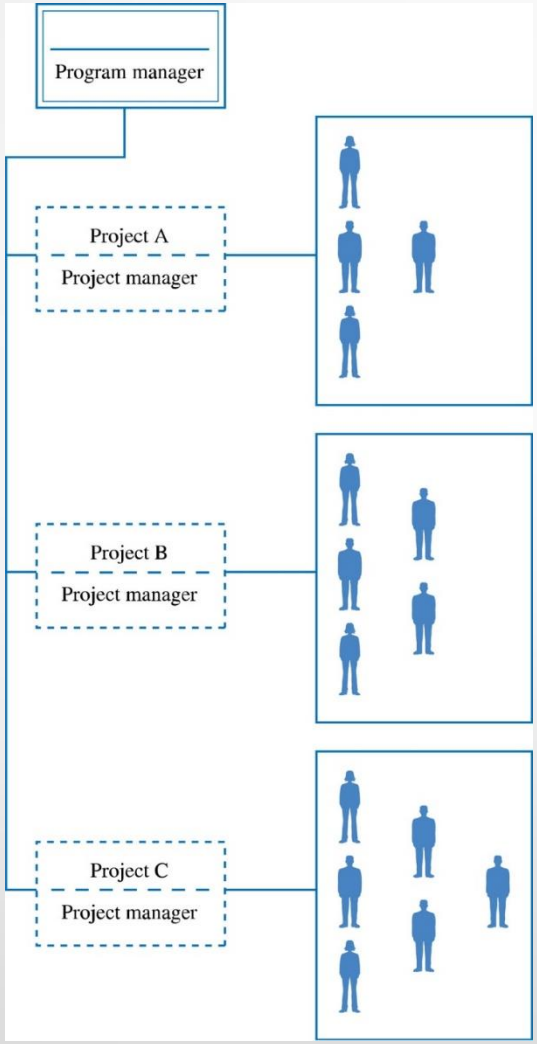

Copyright 2012 John Wiley & Sons, Inc.

THE PROJECT-BASED ORGANIZATION

Advantages

- Clear Authority & Responsibility
- Improved Communication
- High Level of Integration

Disadvantages

- Project Isolation
- Duplication of Effort
- "Projectitis"

Copyright 2012 John Wiley & Sons, Inc.

The Matrix Organization

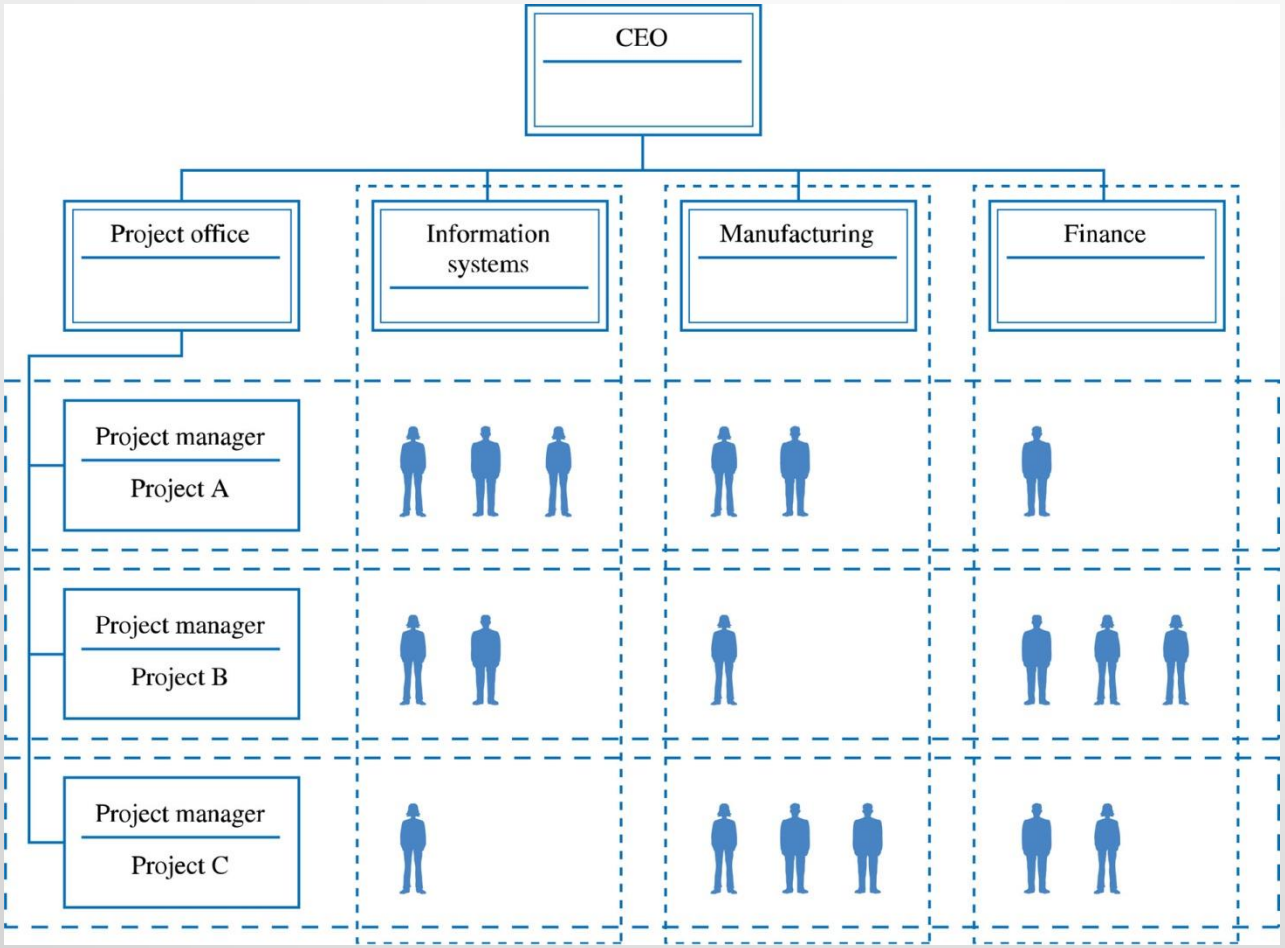

Copyright 2012 John Wiley & Sons, Inc.

THE MATRIX ORGANIZATION

Advantages

- High Level of Integration
- Improved Communication
- Increased Project Focus

Disadvantages

- Potential for conflict
- Unity of Command can be violated
- Poor Response Time

Copyright 2012 John Wiley & Sons, Inc.

formal organizational structure

Relationships

- Formal organization tells us
- how individuals or groups within an organization
- *should* relate to one another

Acutality

- it **does not** tell us
- how they *actually* relate.

Copyright 2012 John Wiley & Sons, Inc.

The Informal Organization

Difference

- Bypasses formal lines of
- communication & authority

Authority

- Power is determined by
- how well one is connected in the informal network
- i.e., the "grapevine"

Complexity

- More complex than formal organizations
- because relationships are established over time

Relationships

- from **positive** and **negative** relationships

Copyright 2012 John Wiley & Sons, Inc.

Stakeholders

«Stake»

- Those having
- a "stake" or claim in the outcome

Pro & Against

- Both are stakeholders:
- In favor of the project's success
- Against the project

Stakeholder Types

- Individuals
- groups
- organizational unit
- a whole organizations

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder Analysis Process

Develop a list of stakeholders

- who have an interest
- in the outcome of the project
- for or against the success!

stakeholder's interest in the project

- "+1" for positive interest
- "0" for neutral
- "-1" for negative interest

Determine the degree of influence

- each stakeholder has on a scale of

Rating

- 0 : no influence
- 10 : can terminate the project

Define a role for each stakeholder

- Champion, consultant, decision maker, ally, rival, foe (opposite), etc.

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder Analysis

objectives of stakeholders

- resource provider
- guidance
- expertise
- acceptance
- approval
- …

Identify a strategy for each stakeholder

- build
- maintain
- improve
- re-establish the relationship

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder	Interest	Influence	Potential Conflicts	Role	Objective	Strategy
Hirem N. Firem	1	5	Competition for resources with other functional managers	Project Sponsor and Champion	Provide resources, approvals, and public support for the project	To maintain open communication so that political landmines can be avoided
Project Team	1	2	This project will change a number of business processes. Affected users may resist change by withholding information	Steve Turner – Network Administrator Shedelle Bivits – Systems Analyst Corean Jenkins – Programmer/DBA Myra Dickens – Inventory Analyst	Provide expertise to complete the project work	Support project team with adequate resources while minimizing distractions
I. Will Sellit	-1	4	As the marketing manager, Sellit is not pleased that this project was chosen over his proposed project. May withhold promised resources	Marketing Manager	Build and maintain best possible relationship to minimize attempts to divert resources	Maintain open communication. Use project sponsor's influence as necessary

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder	Interest	Influence	Potential Conflicts	Role	Objective	Strategy
Hirem N. Firem	1	5	Competition for resources with other functional managers	Project Sponsor and Champion	Provide resources, approvals, and public support for the project	To maintain open communication so that political landmines can be avoided
Dee Manitger	1	3	Resources not made available as promised by functional managers	Project Manager	Lead and manage the project so that it achieves its MOV	Work closely with project stakeholders and project team
Project Team	1	2	This project will change a number of business processes. Affected users may resist change by withholding information	Shedelle Bivits – Systems Analyst Corean Jenkins – Programmer/DBA Myra Dickens – Inventory Analyst		minimizing distractions
I. Will Sellit	-1	4	As the marketing manager, Sellit is not pleased that this project was chosen over his proposed project. May withhold promised resources	Marketing Manager	Build and maintain best possible relationship to minimize attempts to divert resources	Maintain open communication. Use project sponsor's influence as necessary

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder	Interest	Influence	Potential Conflicts	Role	Objective	Strategy
			Competition for resources	Project Sponsor and	Provide resources,	To maintain open communication so that
Project Team	1	2	This project will change a number of business processes. Affected users may resist change by withholding information	Steve Turner – Network Administrator	Provide expertise to complete the project work	Support project team with adequate resources while minimizing distractions
				Shedelle Bivits – Systems Analyst		
				Corean Jenkins – Programmer/DBA		
				Myra Dickens – Inventory Analyst		
I. Will Sellit	-1	4	As the marketing manager, Sellit is not pleased that this project was chosen over his proposed project. May withhold promised resources	Marketing Manager	Build and maintain best possible relationship to minimize attempts to divert resources	Maintain open communication. Use project sponsor's influence as necessary

Copyright 2012 John Wiley & Sons, Inc.

Stakeholder	Interest	Influence	Potential Conflicts	Role	Objective	Strategy
Hirem N. Firem	1	5	Competition for resources with other functional managers	Project Sponsor and Champion	Provide resources, approvals, and public support for the project	To maintain open communication so that political landmines can be avoided
Dee Manitger	1	3	Resources not made available as promised by functional managers	Project Manager	Lead and manage the project so that it achieves its MOV	Work closely with project stakeholders and project team
Project Team	1	2	This project will change a number of business processes. Affected users may resist change by withholding information	Steve Turner – Network Administrator Shedelle Bivits – Systems Analyst Corean Jenkins – Programmer/DBA Myra Dickens – Inventory	Provide expertise to complete the project work	Support project team with adequate resources while minimizing distractions
I. Will Sellit	-1	4	As the marketing manager, Sellit is not pleased that this project was chosen over his proposed project. May withhold promised resources	Marketing Manager	Build and maintain best possible relationship to minimize attempts to divert resources	Maintain open communication. Use project sponsor's influence as necessary

Copyright 2012 John Wiley & Sons, Inc.

The Project Team

Project Manager

- The Roles of the PM:
  - Managerial role
  - Leadership role

Attributes of a successful PM

- ability to communicate with people
- ability to deal with people
- ability to create and sustain relationships
- ability to organize

Copyright 2012 John Wiley & Sons, Inc.

The Wisdom of Teams - Jon R. Katzenbach
Douglas K. Smith

- Work Groups
- Pseudo Teams
- Potential Teams
- Real Teams
- High Performance Teams

Copyright 2012 John Wiley & Sons, Inc.

Work Groups

Members interact to share

- information,
- best practices,
- ideas

Basic Characteristics

- No shared performance goals (individual
- No joint work-products
- No mutual accountability
- Viable in many situations

Example

- study group

Copyright 2012 John Wiley & Sons, Inc.

Teams

Bring

- complementary skills & experience

Jointly defined

- clear goals & approaches
- improve communication

Improve decision-making

Have more fun

Copyright 2012 John Wiley & Sons, Inc.

Traditional Teams

Face-value

- Accept background information
- at "face-value"

Logical linear fashion

- Approach projects in logical, linear fashion

Run-of-the-mill

- Provide run-of-the-mill solutions

Solutions remain

- within the original "frame"
- how the problem was originally presented to them

Copyright 2012 John Wiley & Sons, Inc.

Radical Teams

Do not accept issues & tasks

- at their "face value"

The way the problem is defined

- may very well be the problem

Unquestioned assumptions

- are surfaced & challenged

Only by digging below the surface

- can we get to the "root"
- so that a meaningful solution can emerge

Copyright 2012 John Wiley & Sons, Inc.

Real Teams



Size

- Small number of people

Skills

- Complementary skills

Purpose

- Committed to a common purpose

Goals

- Common goals

Behaviour

- Common approach

Responsibility

- Hold themselves accountable

Copyright 2012 John Wiley & Sons, Inc.

Pseudo Teams

Weak

- Weakest of all groups

No collective performance

- Not focused on collective performance
- & not trying to achieve it

No common purpose

- No interest in shaping a common purpose

Behaviour

- Confusion & dysfunctional behaviours

Copyright 2012 John Wiley & Sons, Inc.

Potential Teams

Potential

- Significant performance potential

Requires more clarity about

- Purpose
- goals
- work-products
- common approach

Copyright 2012 John Wiley & Sons, Inc.

High Performance Teams

Real team

- Meet all the conditions of a real team

PLUS:

- Members are deeply committed
- Perform above all reasonable expectations

Copyright 2012 John Wiley & Sons, Inc.

Project Team Basics

Themes & Identity

Enthusiasm & Energy Level

Event-Driven Histories

Personal Commitment

Earned Membership

Copyright 2012 John Wiley & Sons, Inc.

Project Manager as aTeam Leader

Acts to

- Clarify purpose & goals
- Build commitment & self confidence
- Strengthen team's collective skills
- Remove external obstacles
- Create opportunities for others

Creates the Project Environment

- Work-space
- Team culture and values
- Project administration
- Ethical Conduct

Copyright 2012 John Wiley & Sons, Inc.

LEARNING CYCLES

Derived from

- educator/philosopher John Dewey (1938)

Used to describe how people learn

- Kolb, 1984;
- Honey & Mumford, 1994

Can be applied to project teams

- Jeris, 1997; Redding, 2000

Copyright 2012 John Wiley & Sons, Inc.

A Learning Cycle

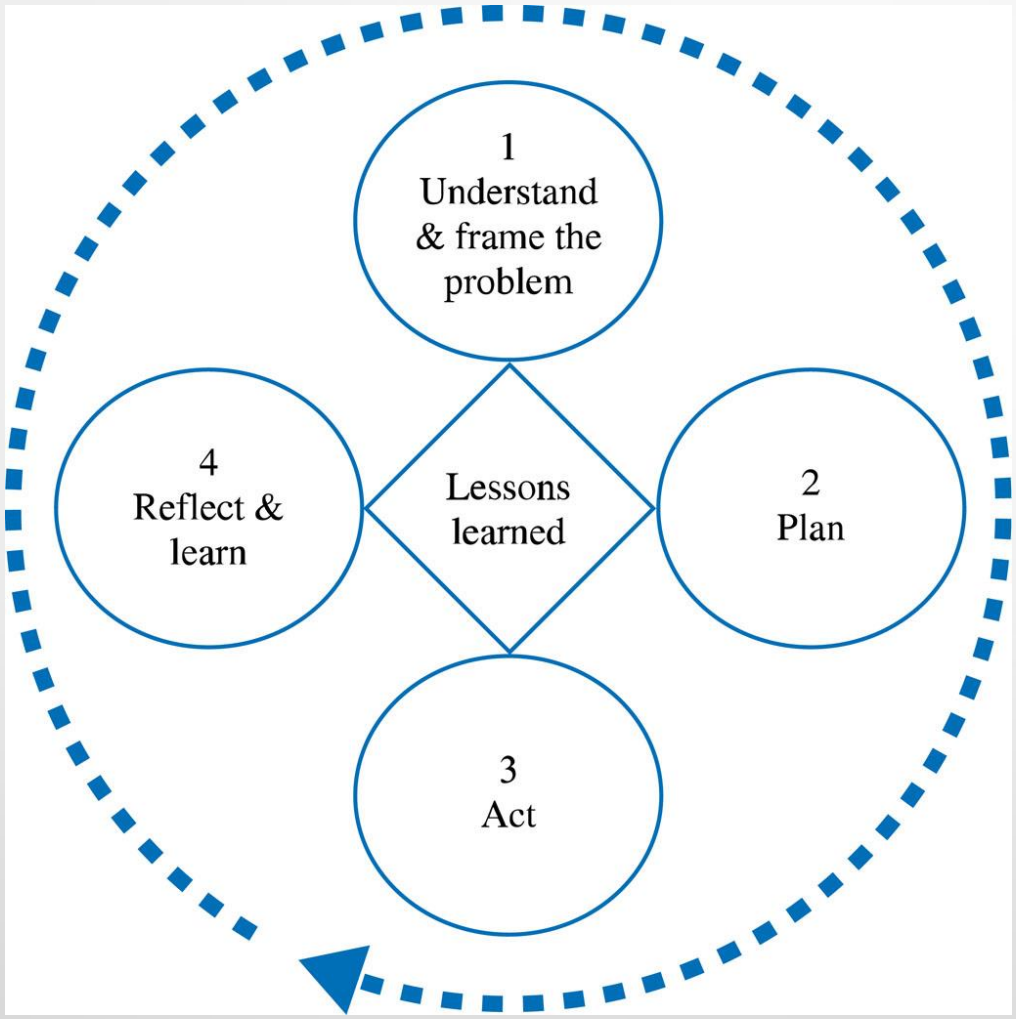

Copyright 2012 John Wiley & Sons, Inc.

Example of a Team Learning Record

Facts	Assumptions	Questions to be Answered
What we know	**What we think we know**	**What we don't know**
Company has too much inventory on hand	It may be an efficiency problem	Why are inventory levels so high?
Cost of maintaining current inventory is becoming prohibitive	Management believes a new information system will improve efficiency and lower inventory levels	What are the current levels of inventory?
Inventory turnover needs to be increased		What is the desired level of inventory?

Copyright 2012 John Wiley & Sons, Inc.

An Example of an Action Plan for Team Learning

Who?	Does What?	By When?
Shedelle & Steve	Interview sales team to understand past, current, and future trends for the company's product.	Tuesday
Myra	Provide a detailed count of the current physical inventory on hand.	Thursday
Corean	Research potential inventory management system commercial packages	Thursday
Steve	Research average inventory levels for the industry	Wednesday

Copyright 2012 John Wiley & Sons, Inc.

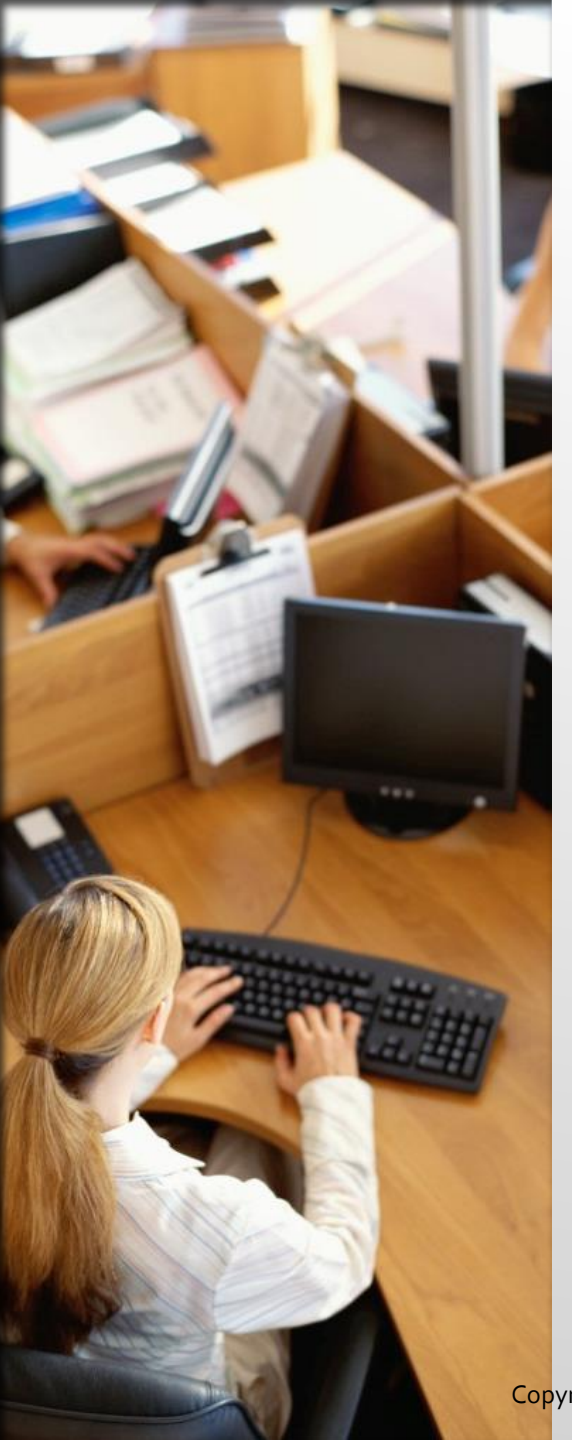

The Project Environment

A place to call home

- Technology
- Office supplies
- Pleasent environment

Culture

- What is expected from each team member?
- What role will each team member play?
- How will conflicts be resolved?

Copyright 2012 John Wiley & Sons, Inc.

Example of a Project Team Charter

Expectations and Team Values

- Everybody's ideas and opinions count
- Everyone must learn something new technically and with the business
- Work hard, but have fun
- Produce necessary, quality periodic deliverables throughout the course of the product
- Add values to clients' organization
- Heavy team commitment
- Show up for team meetings
- Team coordination
- Accountability
- Assistance
- Communication with clients and team
- No such thing as a stupid question
- *RESPECT for everyone*
- Research: expanding knowledge base as well as comfort zone
- Extend ourselves (Leave our comfort zones)
- Punctuality and group attendance
- Equal contributions from members
- Be prepared for meetings: check e-mail and team web site before every meeting
- Trust one another

Grievance Resolution

- Try to resolve issue with each team member first

Copyright 2012 John Wiley & Sons, Inc.

Self Assessment

- Asses what you got so far!

Noticible Issues	Interesting Details	Unclarified issues
What are the noticible issues in this chapter	What is the most interesting details in this chapter?	What are the points need further explanations?

Copyright 2012 John Wiley & Sons, Inc.

Copyright 2012 John Wiley & Sons, Inc.
All rights reserved. Reproduction or translation of this work beyond that permitted in section 117 of the 1976 United States Copyright Act without express permission of the copyright owner is unlawful. Request for further information should be addressed to the Permissions Department, John Wiley & Sons, Inc. The purchaser may make back-up copies for his/her own use only and not for distribution or resale. The Publisher assumes no responsibility for errors, omissions, or damages caused by the use of these programs or from the use of the information herein.
